


ID	Task Name	Duration	Start	Finish	12, '20	Feb 16, '20	Mar 22, '20	Apr 26, '20	May 31, '20	Jul 5, '20	Aug 9, '20	Sep 13, '20	Oct 18, '20	Nov 22, '20	Dec 27, '20	Jan 31, '21	Mar 7, '21	Apr	
					W	T	F	S	S	M	T	W	T	F	S	S	M	T	W
1	<b>Jordanelle-Midway 138kV UG Line</b>	<b>324.25 days</b>	<b>Thu 3/5/20</b>	<b>Tue 3/23/21</b>															
2	<b>Preconstruction</b>	<b>133 days</b>	<b>Thu 3/5/20</b>	<b>Tue 8/4/20</b>															
3	Bid Submittal	0 days	Thu 3/5/20	Thu 3/5/20															
4	Proposal Review	28 days	Thu 3/5/20	Sat 4/4/20															
5	Award Notification	0 days	Sat 4/4/20	Sat 4/4/20															
6	Submittals	3 wks	Sat 4/4/20	Wed 4/22/20															
7	Submittal Approvals	2 wks	Wed 4/22/20	Sat 5/2/20															
8	Material Procurement - Cable	16 wks	Sat 5/2/20	Tue 8/4/20															
9	<b>Construction</b>	<b>247 days</b>	<b>Mon 6/1/20</b>	<b>Tue 3/23/21</b>															
10	Mobilization	1 day	Mon 6/1/20	Mon 6/1/20															
11	Civil, ductbank, vault installation by subcontractor	132 days	Tue 6/2/20	Fri 10/30/20															
12	Pull UG cables by Wasatch, supervision by cable	70 days	Thu 8/27/20	Sat 11/14/20															
13	Terminations, splices, arrestors, grounding	100 days	Sat 11/14/20	Mon 3/22/21															
14	Demobilization	1 day	Mon 3/22/21	Tue 3/23/21															

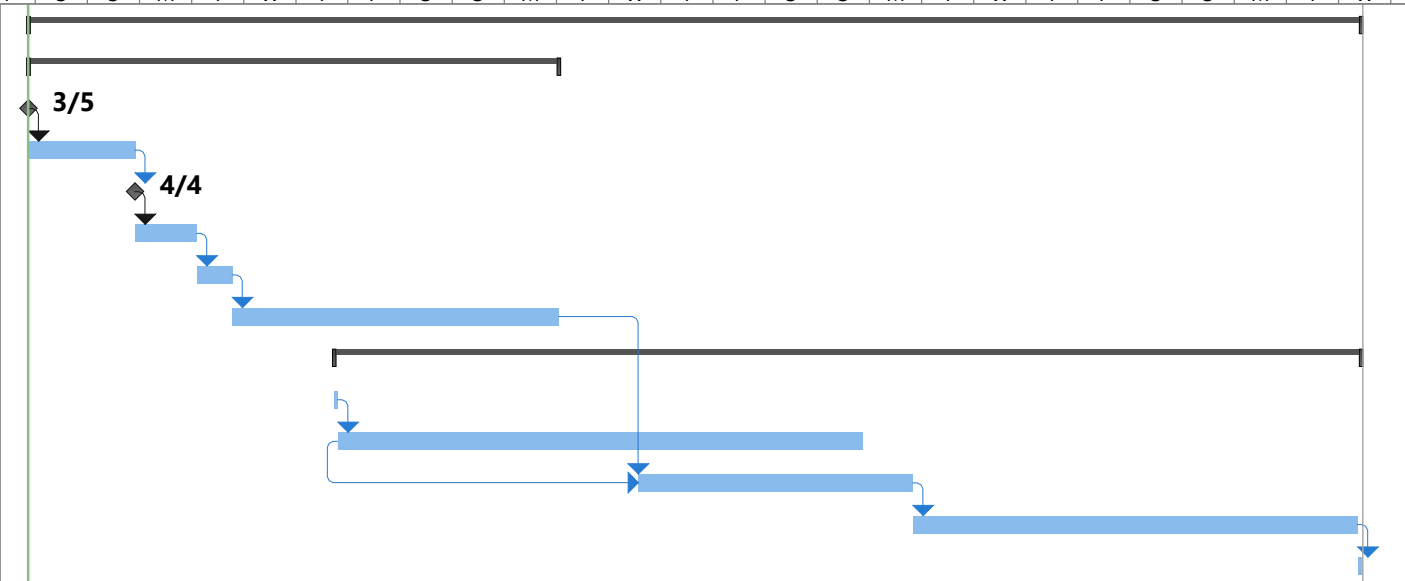

Project: Project Schedule - Jord Date: Thu 3/5/20	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			
