



Empire Electric Association, Inc

801 N. Broadway P.O. Drawer K Cortez, CO 81321-0676 Phone (970) 565-4444

www.EmpireElectric.org

Electrical Service Construction Requirements

Service

Service Order Number	212222
Applicant (person or entity to receive electric bills)	Musumeci, Joseph A
Service Address	797 E. Pioneer Bend
Use of Service	House

Cost

Total Estimated Construction Cost	\$7,959.60
Portion Paid by Empire Electric	\$3,528.07
Applicant Portion	\$4,431.53
Cost Share	\$0.00
Standard Construction Allowance	\$500.00
Share of Construction Cost to be Paid by Applicant	\$3,931.53
Billing Deposit	\$0.00
Total Amount Due Prior to Construction Scheduling	\$3,931.53

Estimated construction costs are for the specified design shown on the enclosed approval form and are valid for six months from the above date. If you want to change the design, we will re-estimate the construction costs and provide a revised approval form for your signature that addresses the agreed upon design.

In addition to all charges shown above, a \$20.00 connect fee will be applied to your first bill for the costs of connecting the service and for setting up the new billing account.

Billing Deposit

There are a number of options available to you in lieu of this cash deposit. If you are interested in using one of these options, contact any consumer records clerk at our office. If a billing deposit is required, it must either be paid along with the construction cost or, if applicable, arrangements must be made prior to construction scheduling.

Requirements to be Completed Before Construction Scheduling

Please return the items checked below that have been included in your information packet.

1. Sign and return the Empire Electric copy of the enclosed contract. Signature(s) on the contract need to match the name(s) on the account as indicated on the top line of the contract. Keep the applicant copy for your records.
2. Sign and return one copy of the enclosed approval form sketch. You need to provide the contractor copy to the appropriate contractors doing trenching and wiring. Keep consumer copy for your records.
3. Sign and return the enclosed easement form. This form requires that all signatures indicated on the form be provided and notarized. This form will be recorded as a public record. Keep the additional copy for your records.
4. Sign and return the enclosed Membership Form. Keep the applicant copy for your records.
5. Please fill out the enclosed applicant information sheet and return it. The form is required for all new members.
6. Provide total amount due as indicated.
7. Other

APPROVAL OF METER AND UNDERGROUND SERVICE LINE LOCATION

Service Address 797 E. PIONEER BEND


Location # 0893950-497600

Map # 85-49

CALL BEFORE YOU DIG --- COLORADO 1-800-922-2987 --- UTAH 1-800-662-4111

Musumeci to provide a 6'x6'x3' deep hole. Empire to install a pad mounted Transformer HERE -

EMPIRE to provide + install a meter pedestal HERE; Musumeci to provide + install EVERYTHING Past the meter

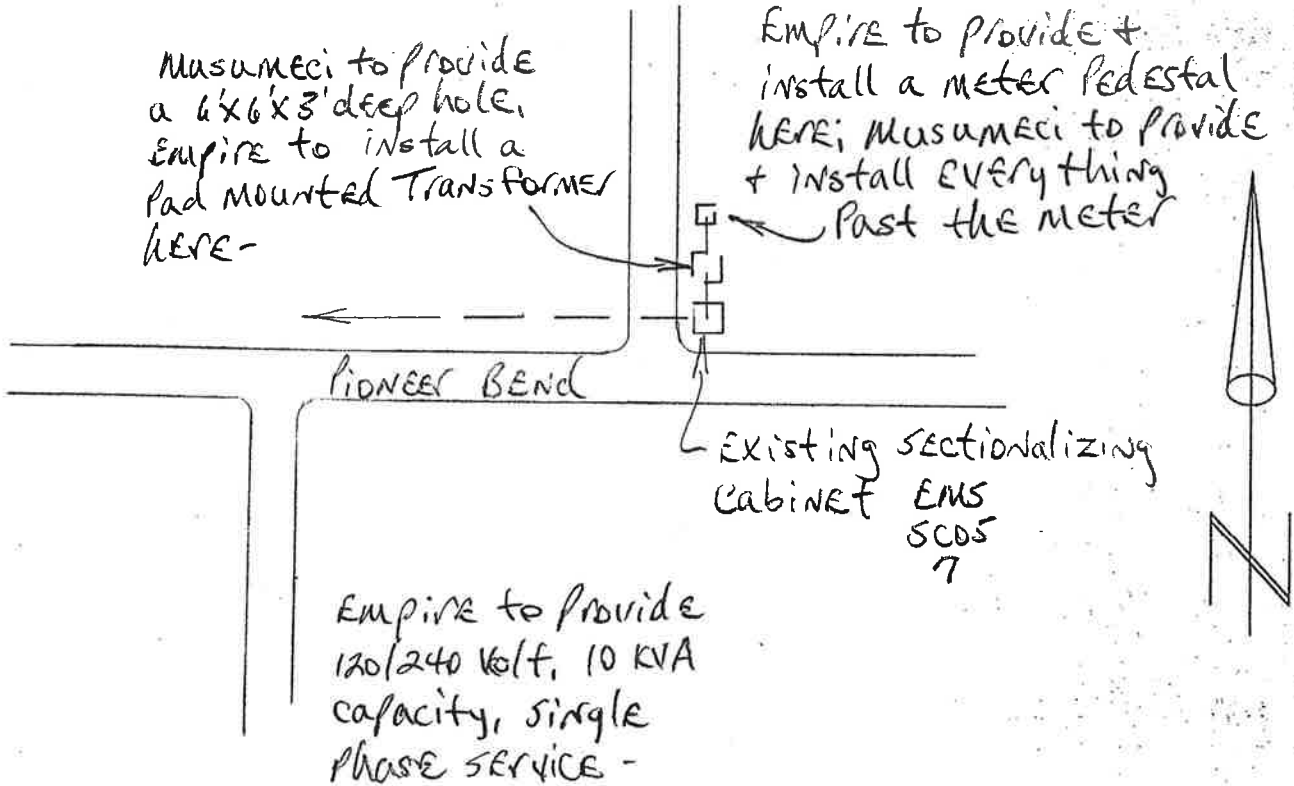

EMPIRE to provide 120/240 Volt, 10 KVA capacity, single phase service -

- All consumer supplied PVC conduit must be GRAY ELECTRICAL GRADE PVC conduit. ←
- EDGE OF ALL TRENCH SPOIL PILES SHALL BE A MINIMUM OF 2 FEET FROM EDGE OF TRENCH. ←

→ SEE DETAIL SKETCH ON BACK

RELAY THIS INFORMATION TO YOUR ELECTRICIAN/CONTRACTOR ←

The consumer or contractor will provide a minimum of 4' foot deep trench on this service extension and will be responsible for providing sand or soft dirt bedding as required. The consumer or contractor will have said trench and required bedding prepared prior to the arrival of Empire Electric crews and will backfill same in the presence of Empire Electric's construction personnel. Any additional crew hours spent due to the failure of the consumer or contractor to comply with the above requirements will be billed to the consumer. Service line will remain unenergized until the trenches are properly backfilled on both sides of the meter and the consumer service beyond the meter has been inspected and approved by the appropriate inspection authority.

I have read and do understand the requirements noted above and agree to the service line and meter location as shown in the above sketch.

11/19/18
Date

[Signature]
Signed


NAME Masumeci

EMPIRE ELECTRIC ASSOCIATION INC
CORTEZ, COLORADO

W.O.# 212222

200 AMP

SINGLE PHASE 200 AMP METERING
FACTORY PEDESTAL MOUNT
SUGGESTED REQUIREMENTS

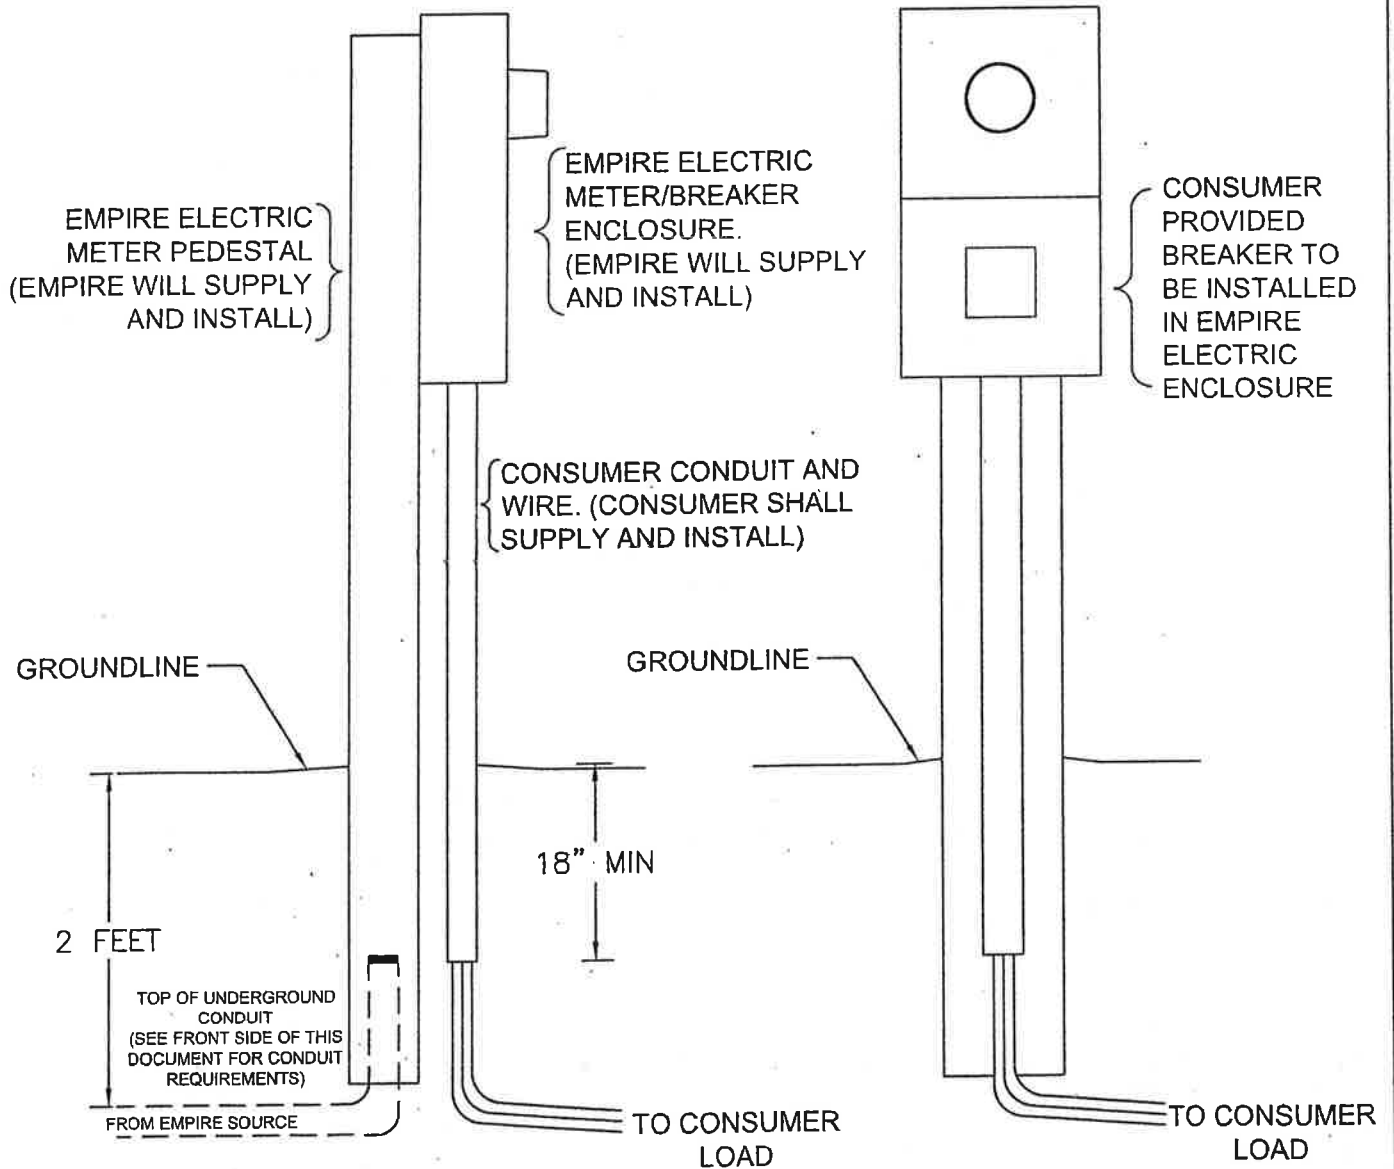

SPECIAL NOTE:
BEFORE SERVICE IS ENERGIZED

All consumer wiring shall be inspected and approved by the appropriate electrical inspector and all trenches shall be completely backfilled!
